


# TCP CHECKLIST 2.0 | July 26, 2021

ACRONYMS	
TCP	Traffic Critical Project
IWZ	Intelligent Work Zone
TIM	Traffic Incident Management
PDMS	Portable Dynamic Message Sign
CCTV	Closed Circuit Television
TMP	Transportation Management Plan

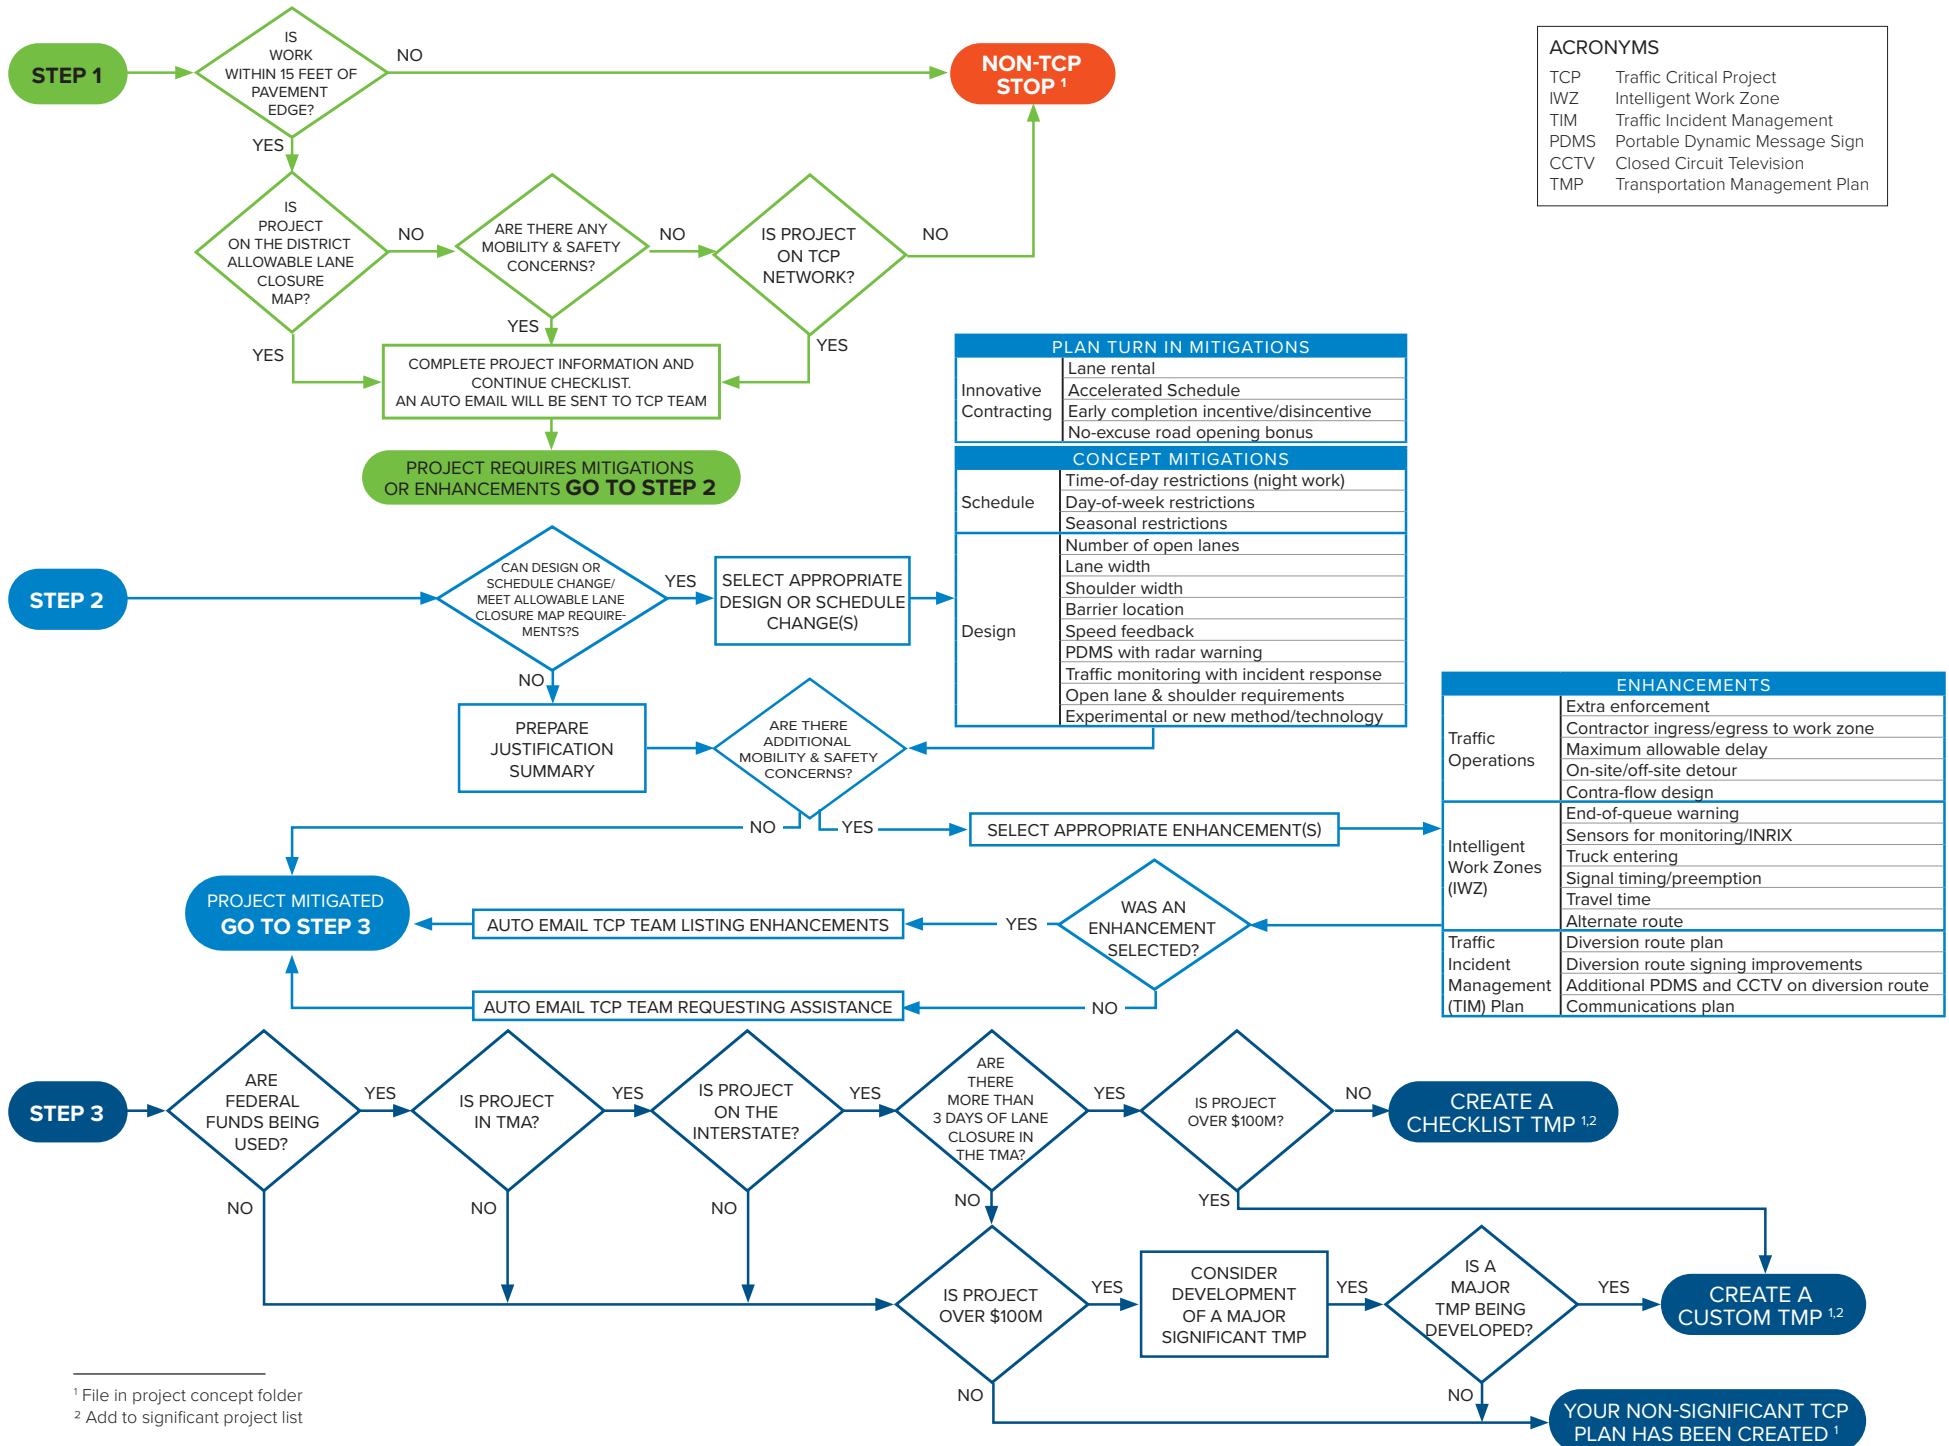

PLAN TURN IN MITIGATIONS	
Innovative Contracting	Lane rental
	Accelerated Schedule
	Early completion incentive/disincentive
	No-excuse road opening bonus
CONCEPT MITIGATIONS	
Schedule	Time-of-day restrictions (night work)
	Day-of-week restrictions
	Seasonal restrictions
Design	Number of open lanes
	Lane width
	Shoulder width
	Barrier location
	Speed feedback
	PDMS with radar warning
	Traffic monitoring with incident response
	Open lane & shoulder requirements
	Experimental or new method/technology

ENHANCEMENTS	
Traffic Operations	Extra enforcement
	Contractor ingress/egress to work zone
	Maximum allowable delay
	On-site/off-site detour
Intelligent Work Zones (IWZ)	Contra-flow design
	End-of-queue warning
	Sensors for monitoring/INRIX
	Truck entering
	Signal timing/preemption
Traffic Incident Management (TIM) Plan	Travel time
	Alternate route
	Diversion route plan
	Diversion route signing improvements
	Additional PDMS and CCTV on diversion route
	Communications plan

<sup>1</sup> File in project concept folder  
<sup>2</sup> Add to significant project list
